




HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

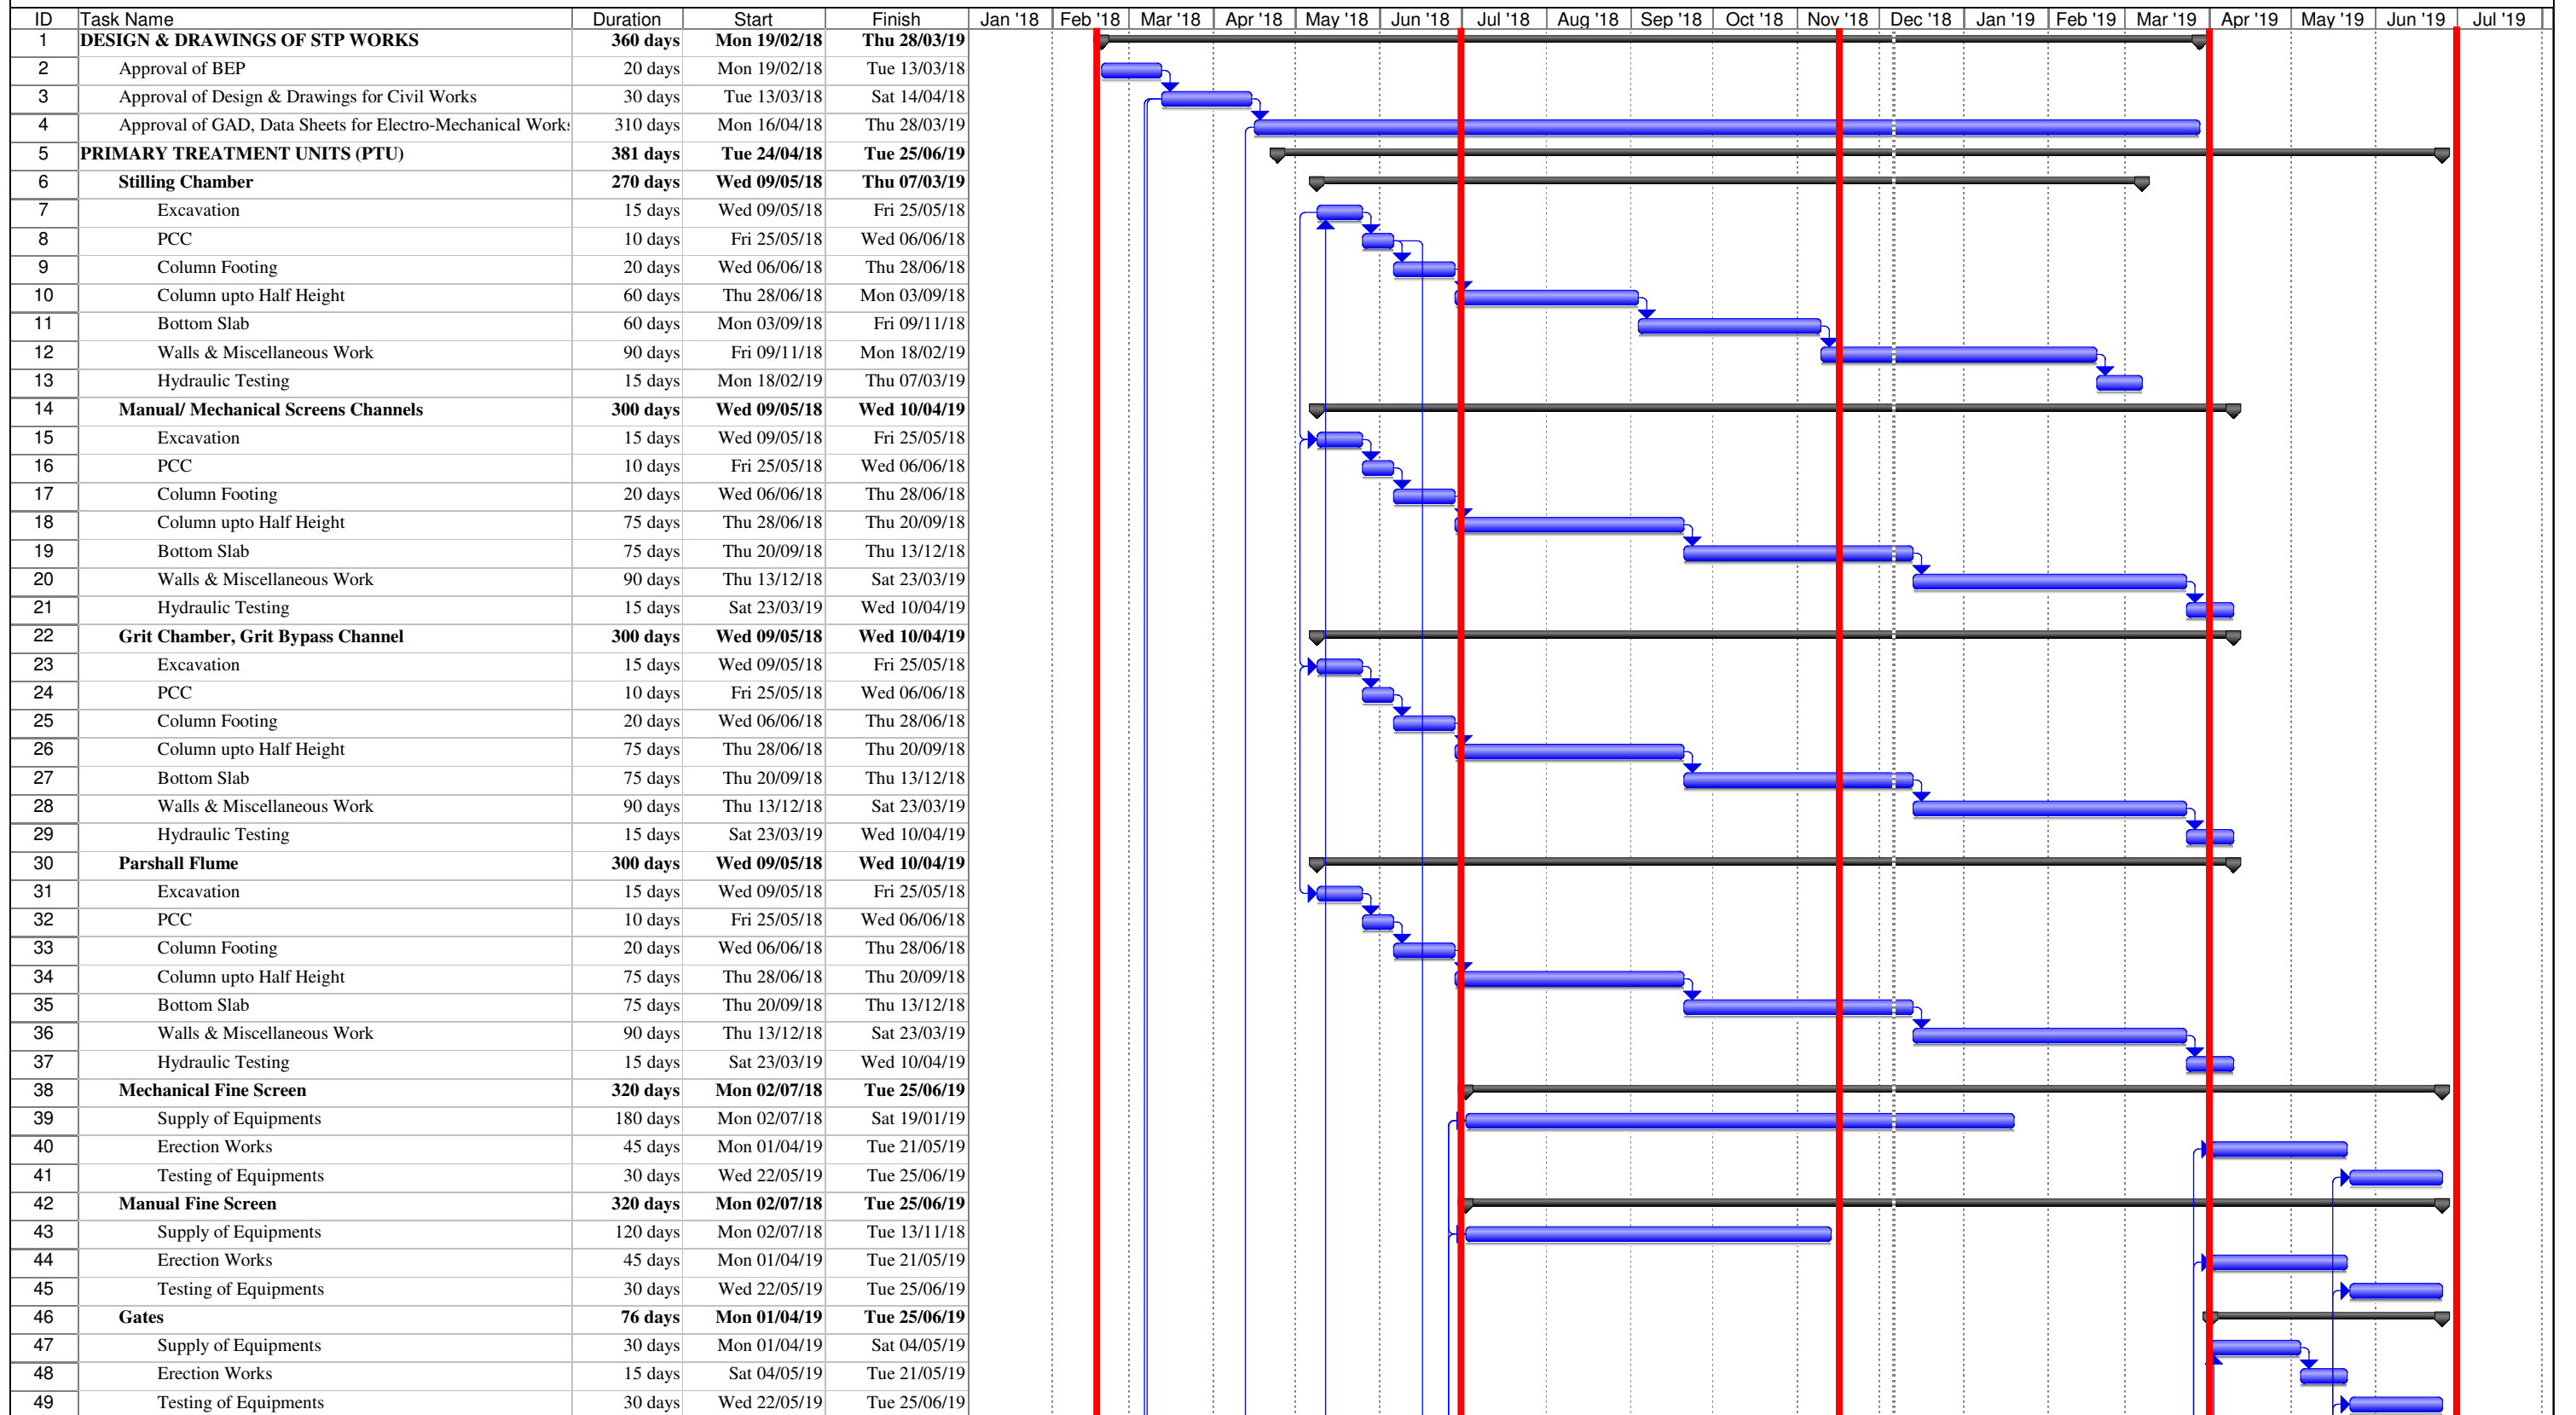

Project: 68 MLD STP@ JAGJEETPUF
Date: Thu 06/12/18


Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

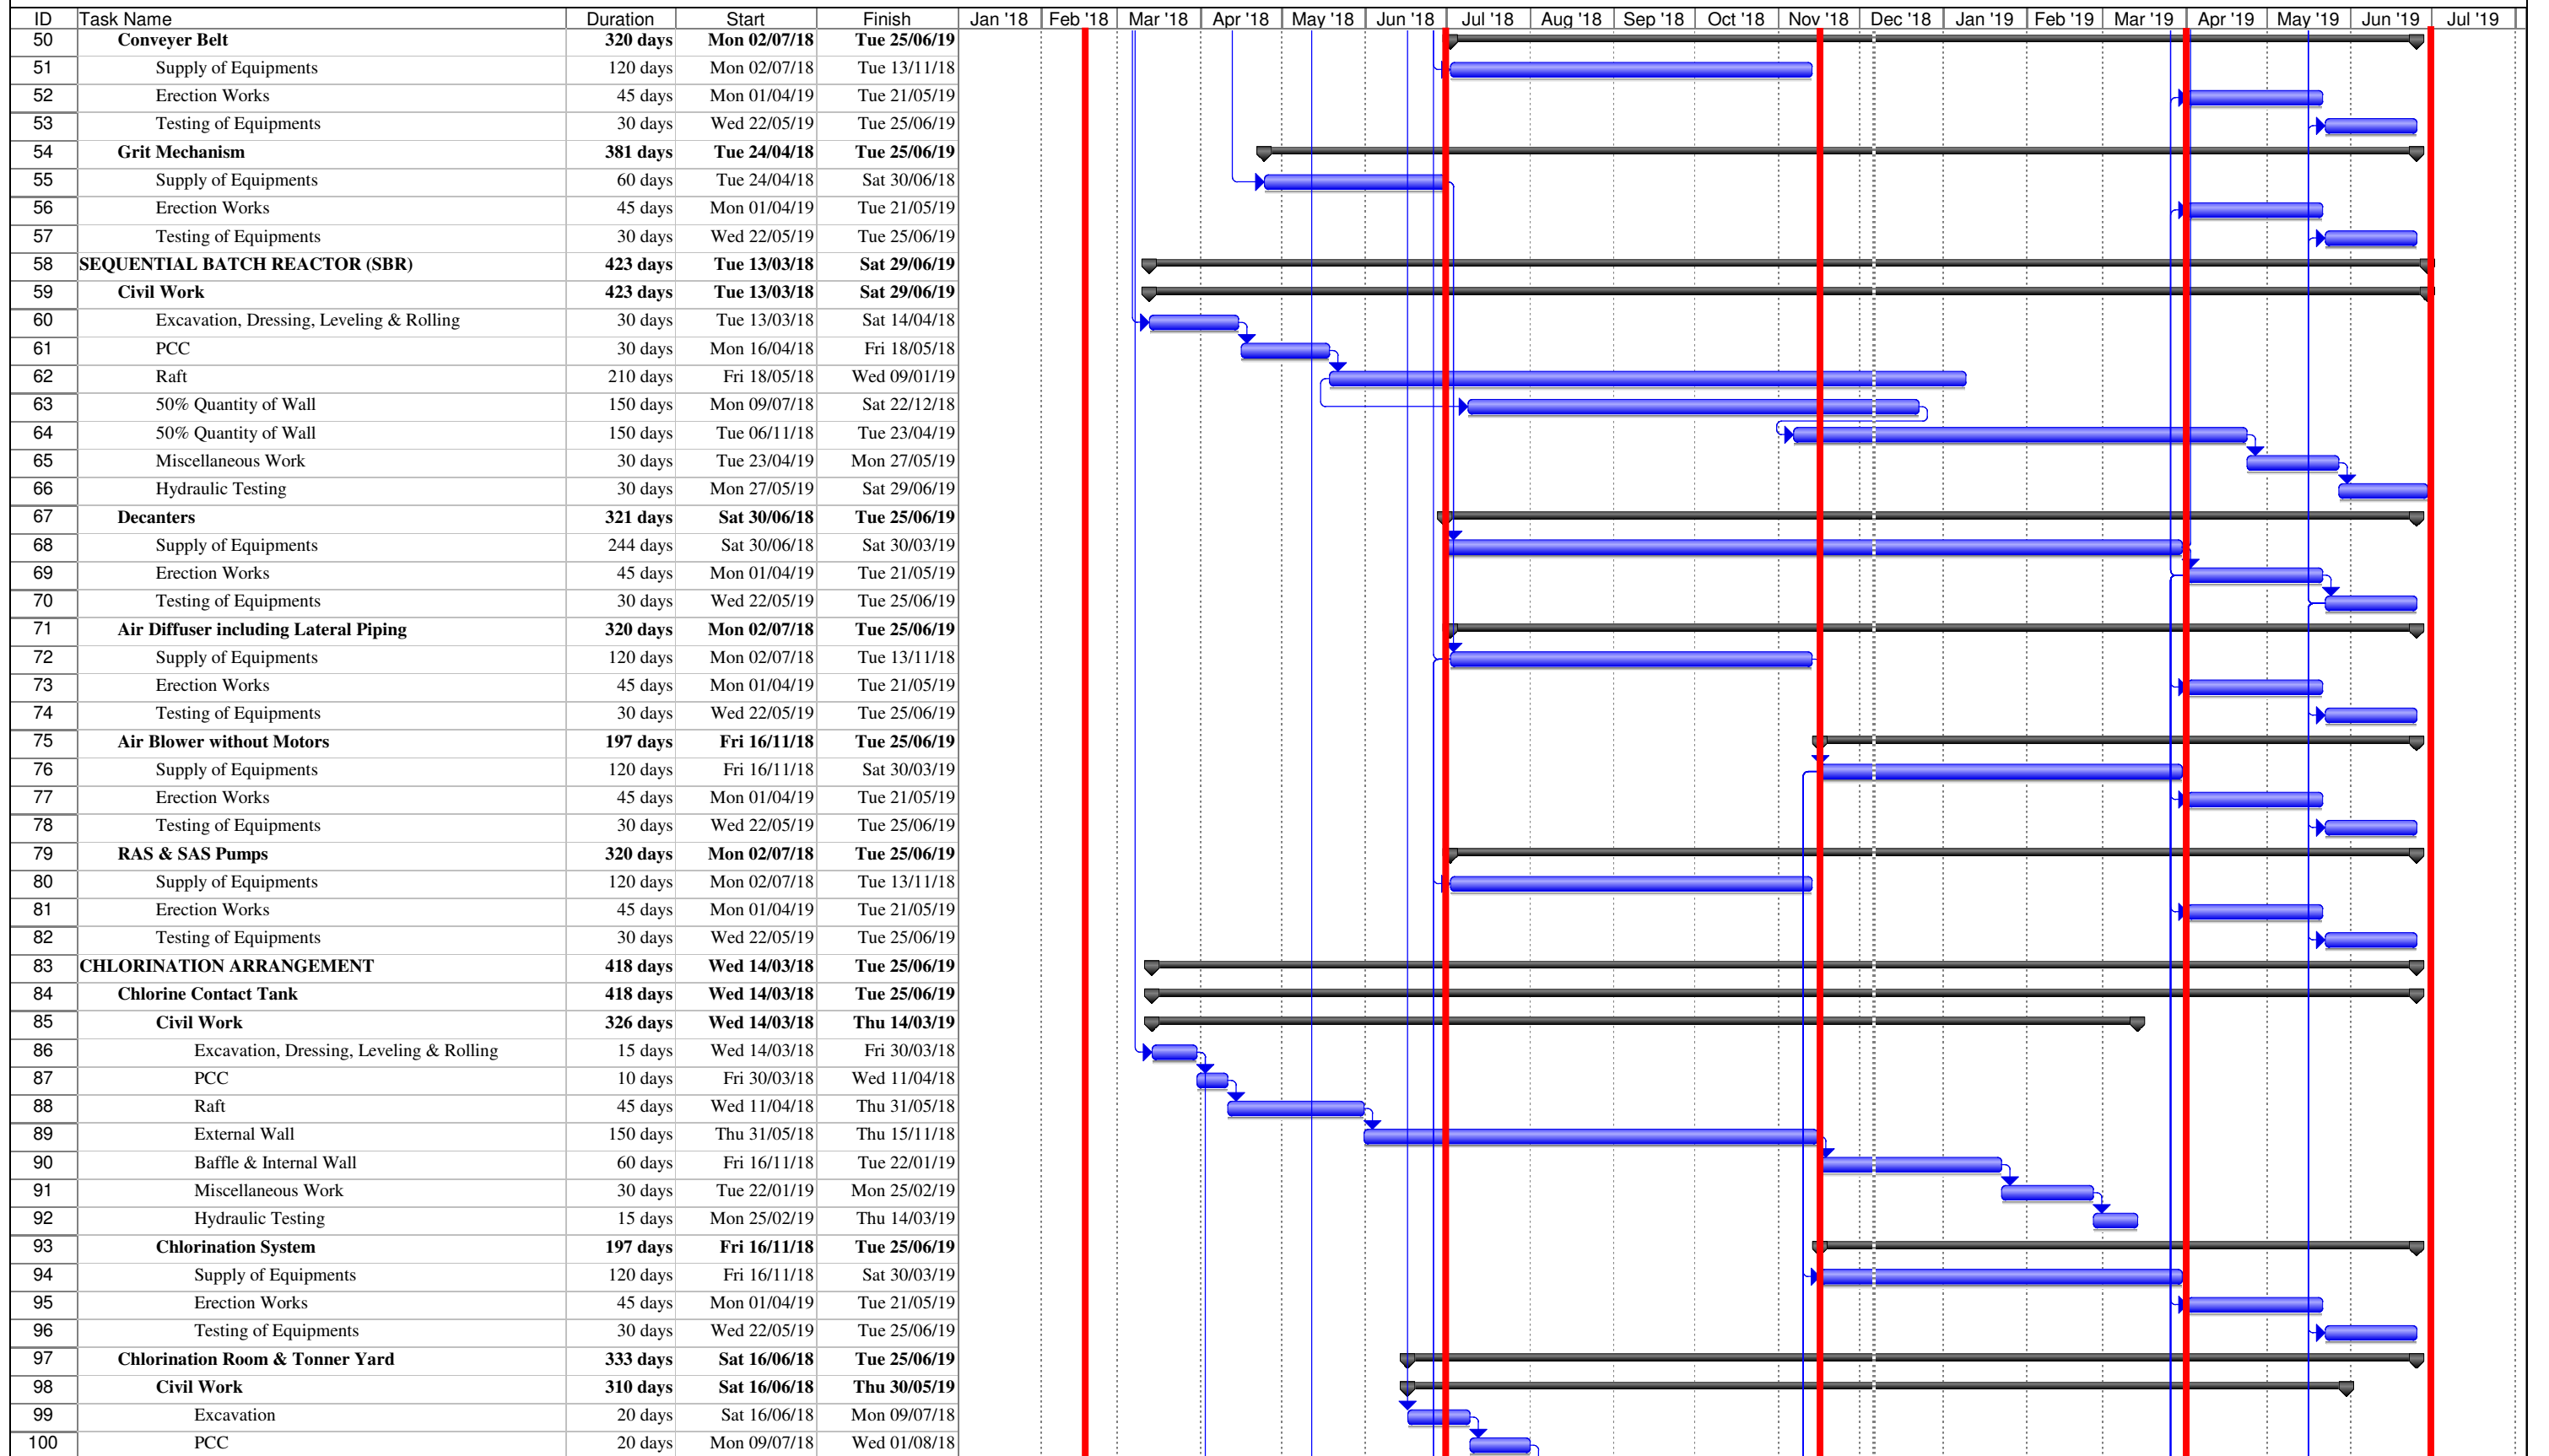

Project: 68 MLD STP@ JAGJEETPUF
Date: Thu 06/12/18

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

ID	Task Name	Duration	Start	Finish	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19	May '19	Jun '19	Jul '19
101	Column upto GL	60 days	Wed 01/08/18	Sat 06/10/18																			
102	Column upto Roof Level	60 days	Sat 06/10/18	Thu 13/12/18																			
103	Roof Slab	60 days	Thu 13/12/18	Mon 18/02/19																			
104	Brick & Plastering Works	60 days	Mon 18/02/19	Fri 26/04/19																			
105	Balance Civil Works	30 days	Fri 26/04/19	Thu 30/05/19																			
106	Chlorine Tonner	197 days	Fri 16/11/18	Tue 25/06/19																			
107	Supply of Equipments	120 days	Fri 16/11/18	Sat 30/03/19																			
108	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
109	Testing of Equipments	30 days	Wed 22/05/19	Tue 25/06/19																			
110	SLUDGE DISPOSAL ARRANGEMENTS	403 days	Fri 30/03/18	Tue 25/06/19																			
111	Sludge Thickner	230 days	Fri 30/03/18	Thu 13/12/18																			
112	Excavation, Dressing, Leveling & Rolling	20 days	Fri 30/03/18	Sat 21/04/18																			
113	PCC	15 days	Sat 21/04/18	Wed 09/05/18																			
114	Raft	45 days	Wed 09/05/18	Thu 28/06/18																			
115	100% wall of Thickner 1	60 days	Mon 11/06/18	Fri 17/08/18																			
116	100% wall of Thickner 2	60 days	Thu 28/06/18	Mon 03/09/18																			
117	Miscellaneous Work	60 days	Mon 03/09/18	Fri 09/11/18																			
118	Hydraulic Testing	30 days	Fri 09/11/18	Thu 13/12/18																			
119	Sludge Thickner Mechanism	320 days	Mon 02/07/18	Tue 25/06/19																			
120	Supply of Equipments	120 days	Mon 02/07/18	Tue 13/11/18																			
121	Erection Works	45 days	Fri 16/11/18	Sat 05/01/19																			
122	Testing of Equipments	30 days	Wed 22/05/19	Tue 25/06/19																			
123	Centrifuge Unit	330 days	Sat 21/04/18	Fri 26/04/19																			
124	Excavation	15 days	Sat 21/04/18	Wed 09/05/18																			
125	PCC	15 days	Wed 09/05/18	Fri 25/05/18																			
126	Column upto GL	30 days	Fri 25/05/18	Thu 28/06/18																			
127	Platform Slab	90 days	Thu 28/06/18	Sat 06/10/18																			
128	Roof Slab	90 days	Sat 06/10/18	Wed 16/01/19																			
129	Brick & Plastering Works	60 days	Wed 16/01/19	Sat 23/03/19																			
130	Balance Civil Works	30 days	Sat 23/03/19	Fri 26/04/19																			
131	Centrifuge	320 days	Mon 02/07/18	Tue 25/06/19																			
132	Supply of Equipments	120 days	Mon 02/07/18	Tue 13/11/18																			
133	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
134	Testing of Equipments	30 days	Wed 22/05/19	Tue 25/06/19																			
135	Centrifuge Feed Pump	197 days	Fri 16/11/18	Tue 25/06/19																			
136	Supply of Equipments	120 days	Fri 16/11/18	Sat 30/03/19																			
137	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
138	Testing of Equipments	30 days	Wed 22/05/19	Tue 25/06/19																			
139	Sludge Sump	180 days	Sat 21/04/18	Fri 09/11/18																			
140	Excavation	15 days	Sat 21/04/18	Wed 09/05/18																			
141	PCC	15 days	Wed 09/05/18	Fri 25/05/18																			
142	Raft	30 days	Fri 25/05/18	Thu 28/06/18																			
143	50% Quantity of Wall	30 days	Thu 28/06/18	Wed 01/08/18																			
144	50% Quantity of Wall	30 days	Wed 01/08/18	Mon 03/09/18																			
145	Miscellaneous Work	30 days	Mon 03/09/18	Sat 06/10/18																			
146	Hydraulic Testing	30 days	Sat 06/10/18	Fri 09/11/18																			
147	Sludge Sump Air Blower without Motors	320 days	Mon 02/07/18	Tue 25/06/19																			
148	Supply of Equipments	120 days	Mon 02/07/18	Tue 13/11/18																			
149	Erection Works	45 days	Fri 16/11/18	Sat 05/01/19																			
150	Testing of Equipments	30 days	Wed 22/05/19	Tue 25/06/19																			

Project: 68 MLD STP@ JAGJEETPUF
Date: Thu 06/12/18


Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

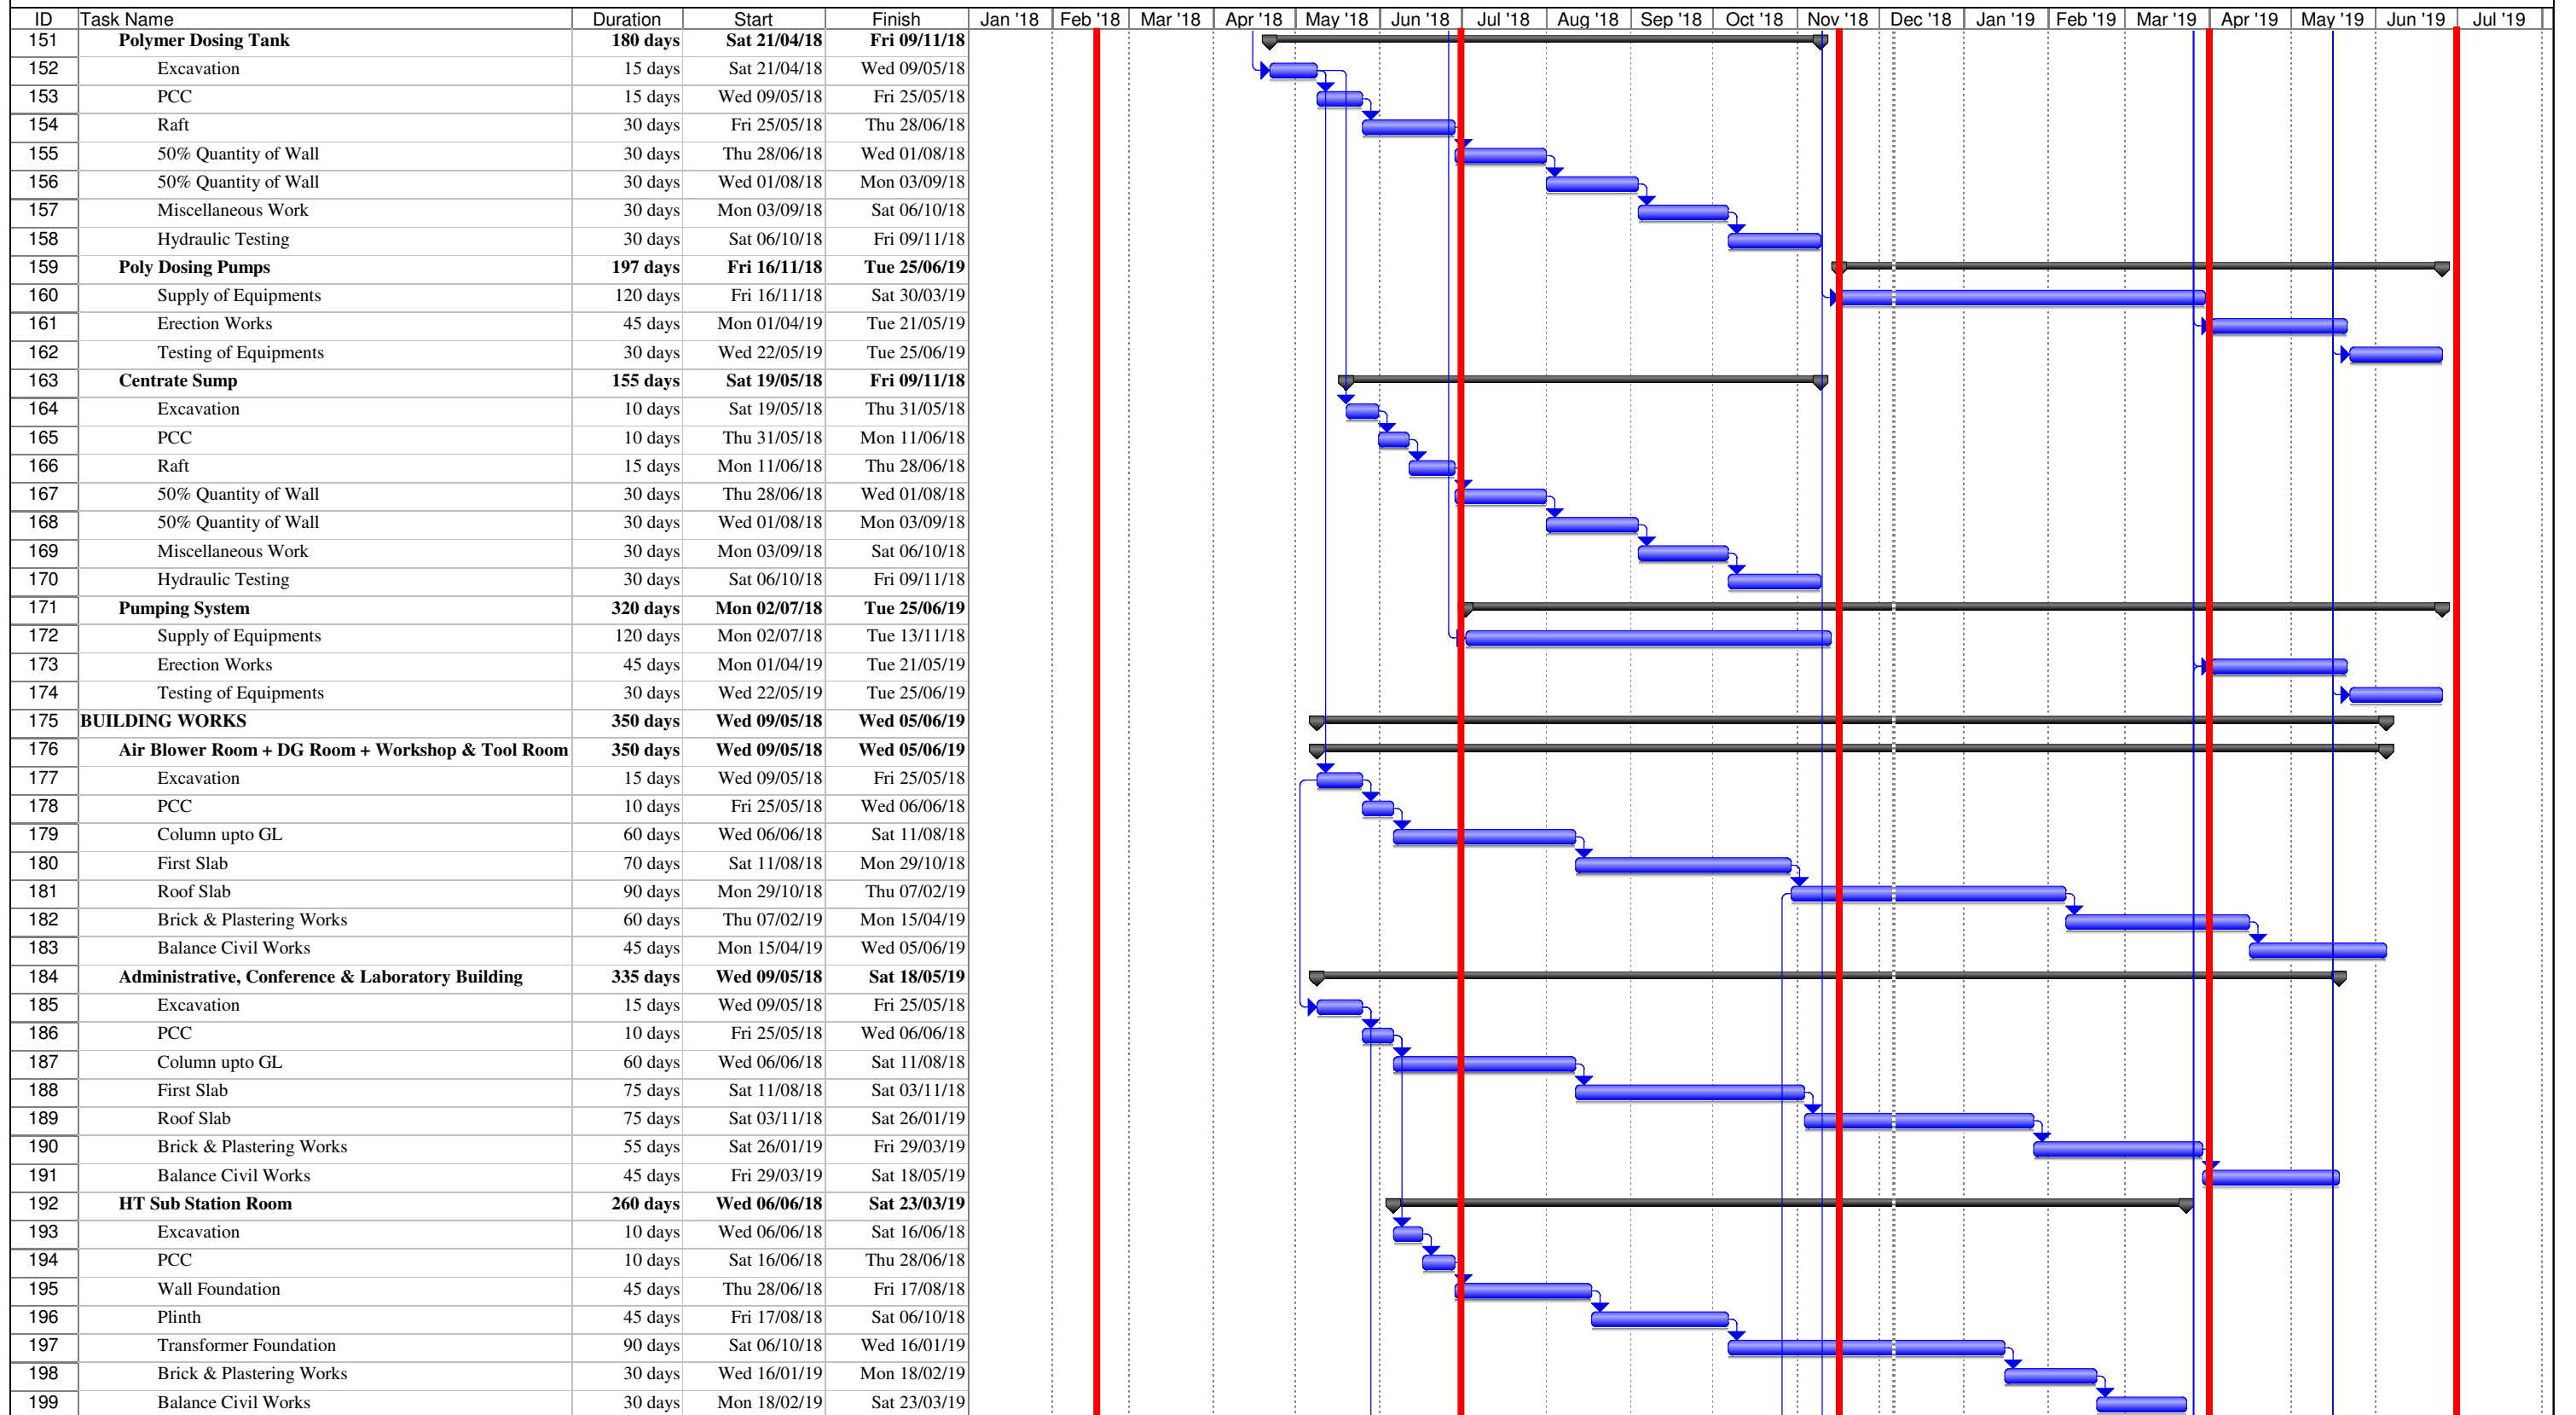

Project: 68 MLD STP@ JAGJEETPUF
Date: Thu 06/12/18

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

ID	Task Name	Duration	Start	Finish	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19	May '19	Jun '19	Jul '19
200	Security Cabin	209 days	Fri 25/05/18	Tue 15/01/19																			
201	Excavation	7 days	Fri 25/05/18	Sat 02/06/18																			
202	PCC	7 days	Sat 02/06/18	Sat 09/06/18																			
203	Column upto GL	15 days	Mon 11/06/18	Wed 27/06/18																			
204	Column upto Slab Level	30 days	Wed 27/06/18	Tue 31/07/18																			
205	Slab	60 days	Tue 31/07/18	Fri 05/10/18																			
206	Brick & Plastering Works	60 days	Fri 05/10/18	Wed 12/12/18																			
207	Balance Civil Works	30 days	Wed 12/12/18	Tue 15/01/19																			
208	MISCELLANEOUS WORKS	176 days	Fri 16/11/18	Sat 01/06/19																			
209	Campus Road	55 days	Mon 01/04/19	Sat 01/06/19																			
210	Sub Base	20 days	Mon 01/04/19	Tue 23/04/19																			
211	WBM	15 days	Tue 23/04/19	Fri 10/05/19																			
212	Top Layer	20 days	Fri 10/05/19	Sat 01/06/19																			
213	Barbed Wire Fencing	150 days	Fri 16/11/18	Fri 03/05/19																			
214	Excavation	25 days	Fri 16/11/18	Fri 14/12/18																			
215	PCC	15 days	Fri 14/12/18	Mon 31/12/18																			
216	Vertical MS Post	25 days	Mon 31/12/18	Mon 28/01/19																			
217	Horizontal Post	25 days	Mon 28/01/19	Mon 25/02/19																			
218	Barbed Wire Fencing	30 days	Mon 25/02/19	Sat 30/03/19																			
219	Balance Civil Works	30 days	Sat 30/03/19	Fri 03/05/19																			
220	Landscaping, Site Development & Plantation	55 days	Mon 01/04/19	Sat 01/06/19																			
221	Landscaping	30 days	Mon 01/04/19	Sat 04/05/19																			
222	Horticulture Development	25 days	Sat 04/05/19	Sat 01/06/19																			
223	ELECTRICAL & INSTRUMENTATION WORKS	197 days	Fri 16/11/18	Tue 25/06/19																			
224	Transformer	197 days	Fri 16/11/18	Tue 25/06/19																			
225	Supply of Machinery / Equipments at Site	120 days	Fri 16/11/18	Sat 30/03/19																			
226	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
227	Testing of Equipment	30 days	Wed 22/05/19	Tue 25/06/19																			
228	DG	76 days	Mon 01/04/19	Tue 25/06/19																			
229	Supply of Machinery / Equipments at Site	30 days	Mon 01/04/19	Sat 04/05/19																			
230	Erection Works	15 days	Sat 04/05/19	Tue 21/05/19																			
231	Testing of Equipment	30 days	Wed 22/05/19	Tue 25/06/19																			
232	LT Panel	76 days	Mon 01/04/19	Tue 25/06/19																			
233	Supply of Machinery / Equipments at Site	30 days	Mon 01/04/19	Sat 04/05/19																			
234	Erection Works	15 days	Sat 04/05/19	Tue 21/05/19																			
235	Testing of Equipment	30 days	Wed 22/05/19	Tue 25/06/19																			
236	Cable & Cable Tray	197 days	Fri 16/11/18	Tue 25/06/19																			
237	Supply of Machinery / Equipments at Site	120 days	Fri 16/11/18	Sat 30/03/19																			
238	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
239	Testing of Equipment	30 days	Wed 22/05/19	Tue 25/06/19																			
240	PLC / SCADA System	197 days	Fri 16/11/18	Tue 25/06/19																			
241	Supply of Machinery / Equipments at Site	120 days	Fri 16/11/18	Sat 30/03/19																			
242	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
243	Testing of Equipment	30 days	Wed 22/05/19	Tue 25/06/19																			
244	Motors for Air Blowers	197 days	Fri 16/11/18	Tue 25/06/19																			
245	Supply of Machinery / Equipments at Site	120 days	Fri 16/11/18	Sat 30/03/19																			
246	Erection Works	45 days	Mon 01/04/19	Tue 21/05/19																			
247	Testing of Equipment	30 days	Wed 22/05/19	Tue 25/06/19																			

Project: 68 MLD STP@ JAGJEETPUF
Date: Thu 06/12/18

Task Progress
Split Milestone

Summary
 Project Summary

External Tasks
 External Milestone

Deadline



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

ID	Task Name	Duration	Start	Finish	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19	May '19	Jun '19	Jul '19
248	INTERCONNECTING PIPING & PIPE FITTINGS WORKS	196 days	Fri 16/11/18	Mon 24/06/19																			
249	RCC Pipes Works	196 days	Fri 16/11/18	Mon 24/06/19																			
250	Supply of Material	120 days	Fri 16/11/18	Sat 30/03/19																			
251	Excavation	45 days	Mon 01/04/19	Tue 21/05/19																			
252	Lowering & Laying	30 days	Tue 21/05/19	Mon 24/06/19																			
253	CI & DI Pipes Works	196 days	Fri 16/11/18	Mon 24/06/19																			
254	Supply of Material	120 days	Fri 16/11/18	Sat 30/03/19																			
255	Excavation	45 days	Mon 01/04/19	Tue 21/05/19																			
256	Lowering & Laying	30 days	Tue 21/05/19	Mon 24/06/19																			
257	Valves & Specials	75 days	Mon 01/04/19	Mon 24/06/19																			
258	Supply of Material	45 days	Mon 01/04/19	Tue 21/05/19																			
259	Excavation	15 days	Tue 21/05/19	Fri 07/06/19																			
260	Lowering & Laying	15 days	Fri 07/06/19	Mon 24/06/19																			

1. Activities shown above may start and finish earlier / later depending on site condition
2. Progress at Site is dependent on timely payment of advance and bill
3. Above Bar Chart is excluding monsoon period

Project: 68 MLD STP@ JAGJEETPUF
Date: Thu 06/12/18

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
