




HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

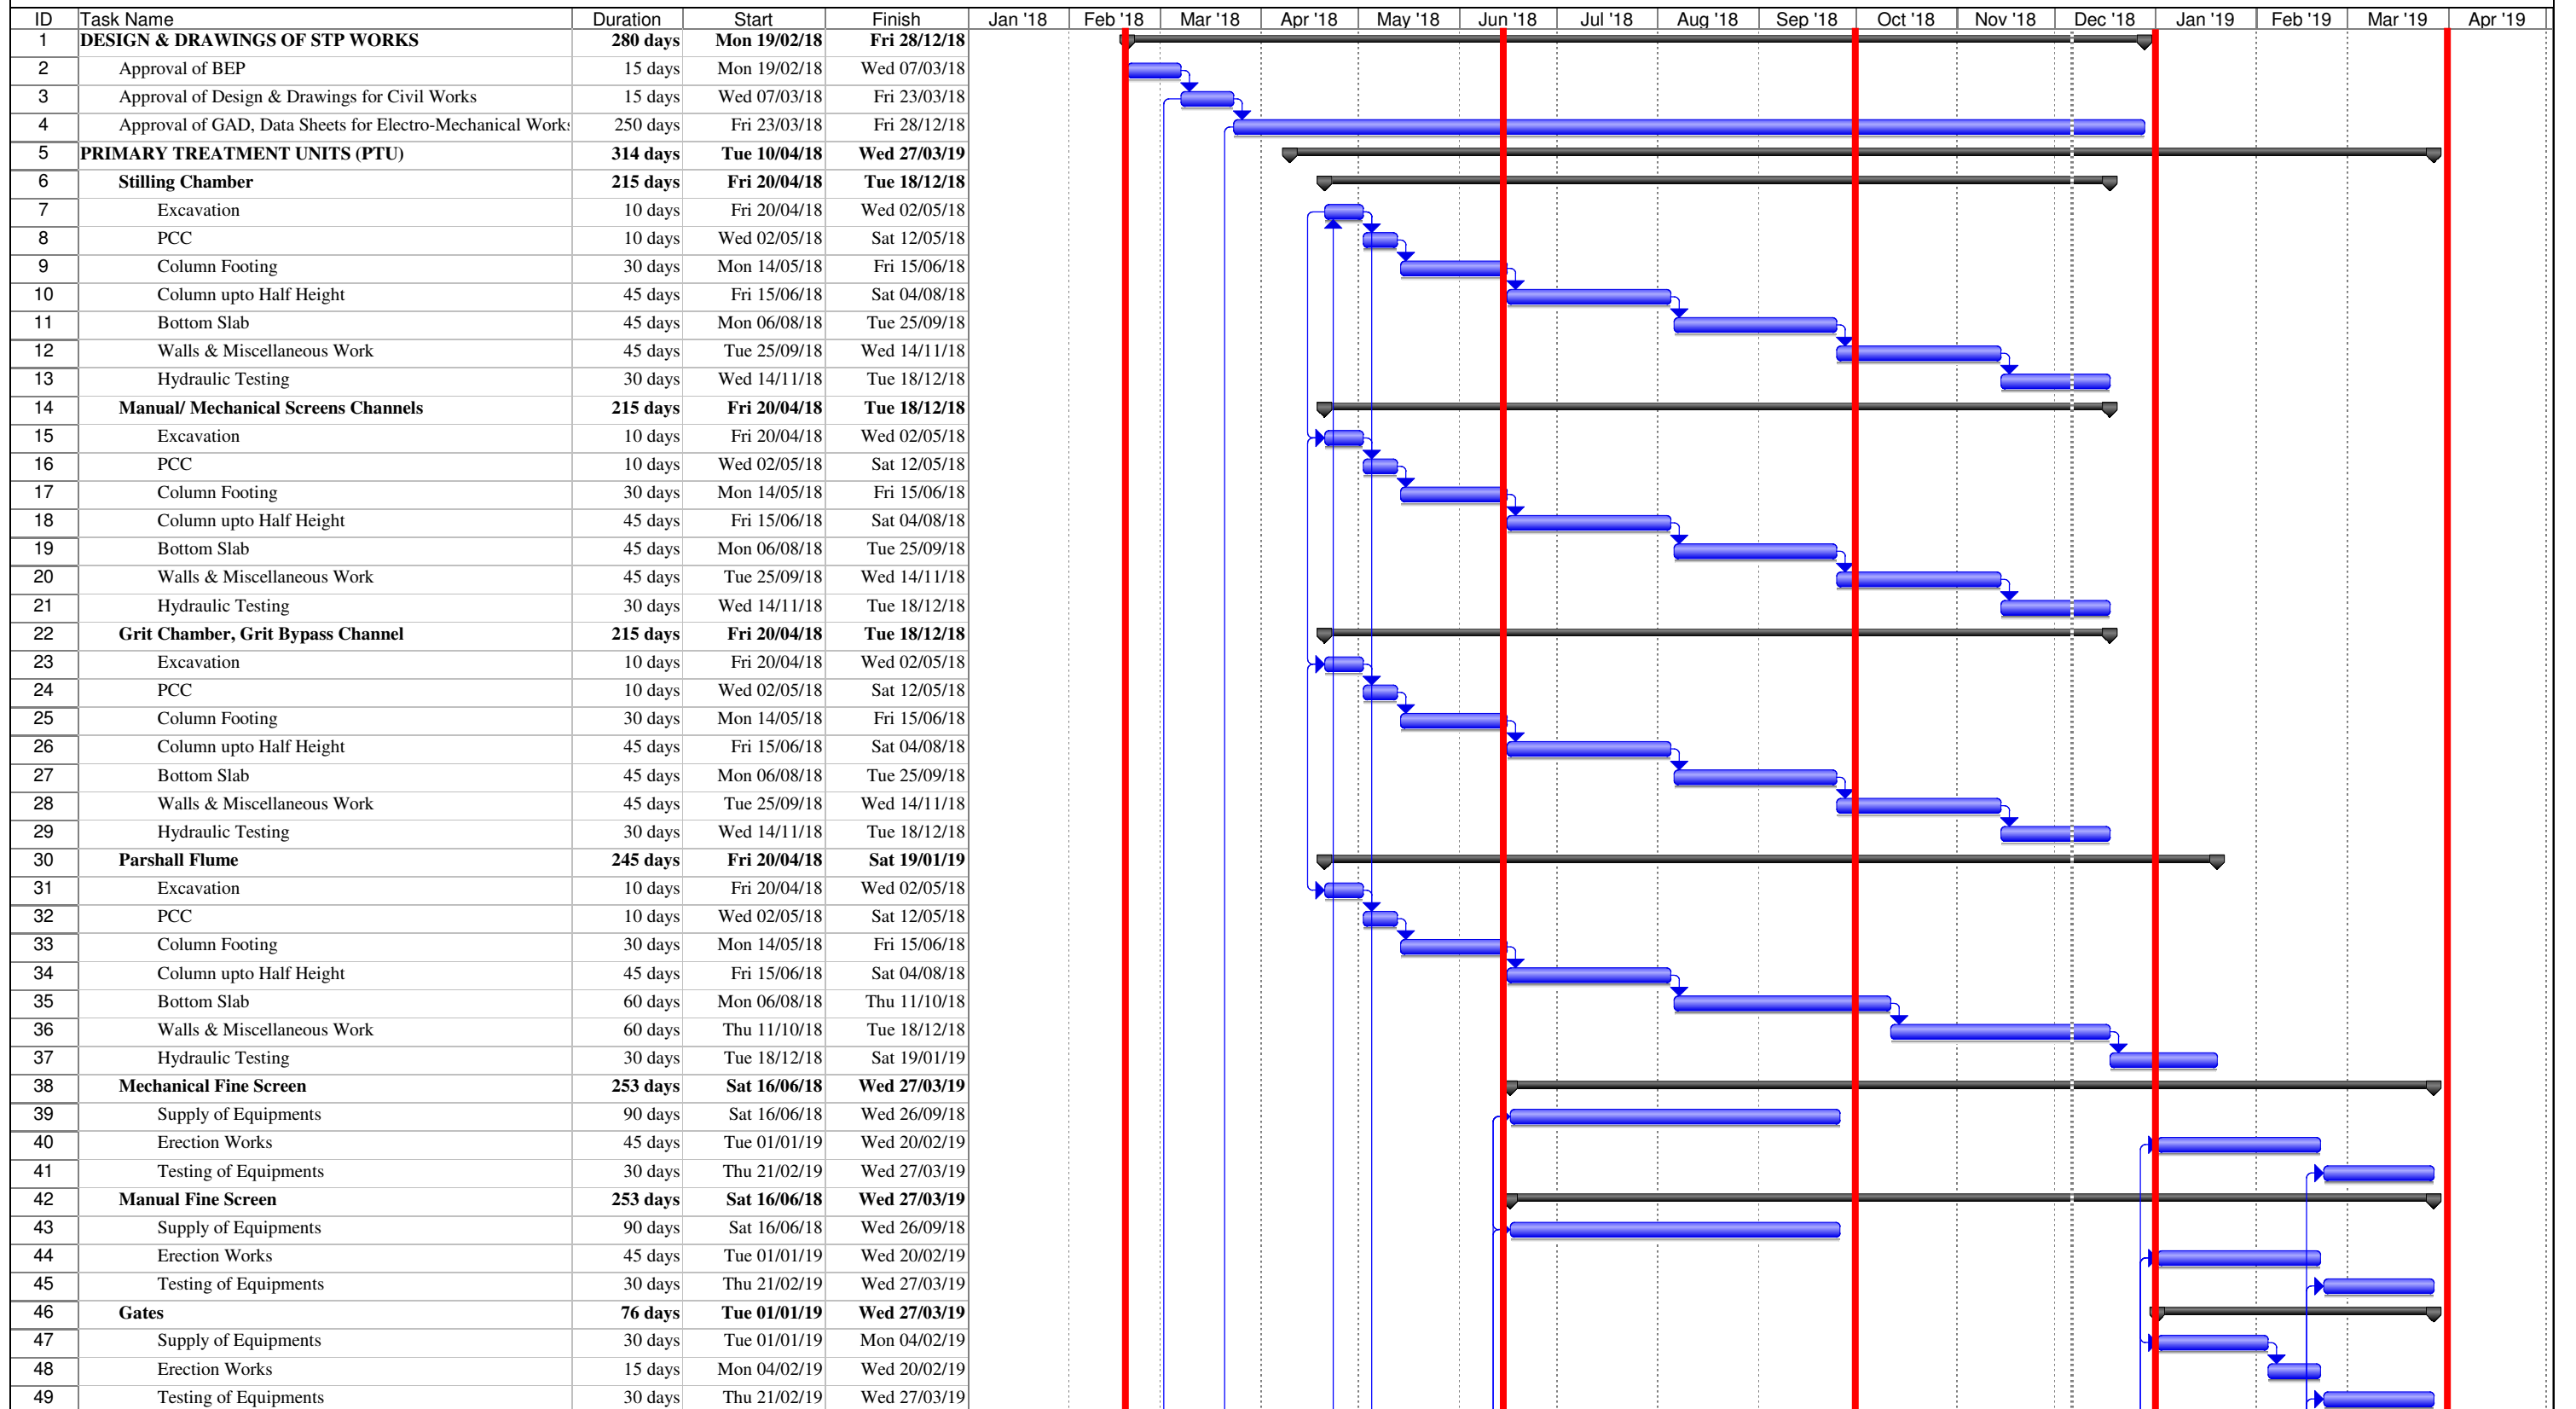

Project: 14 MLD STP@ SARAI HARIC
Date: Thu 06/12/18


Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

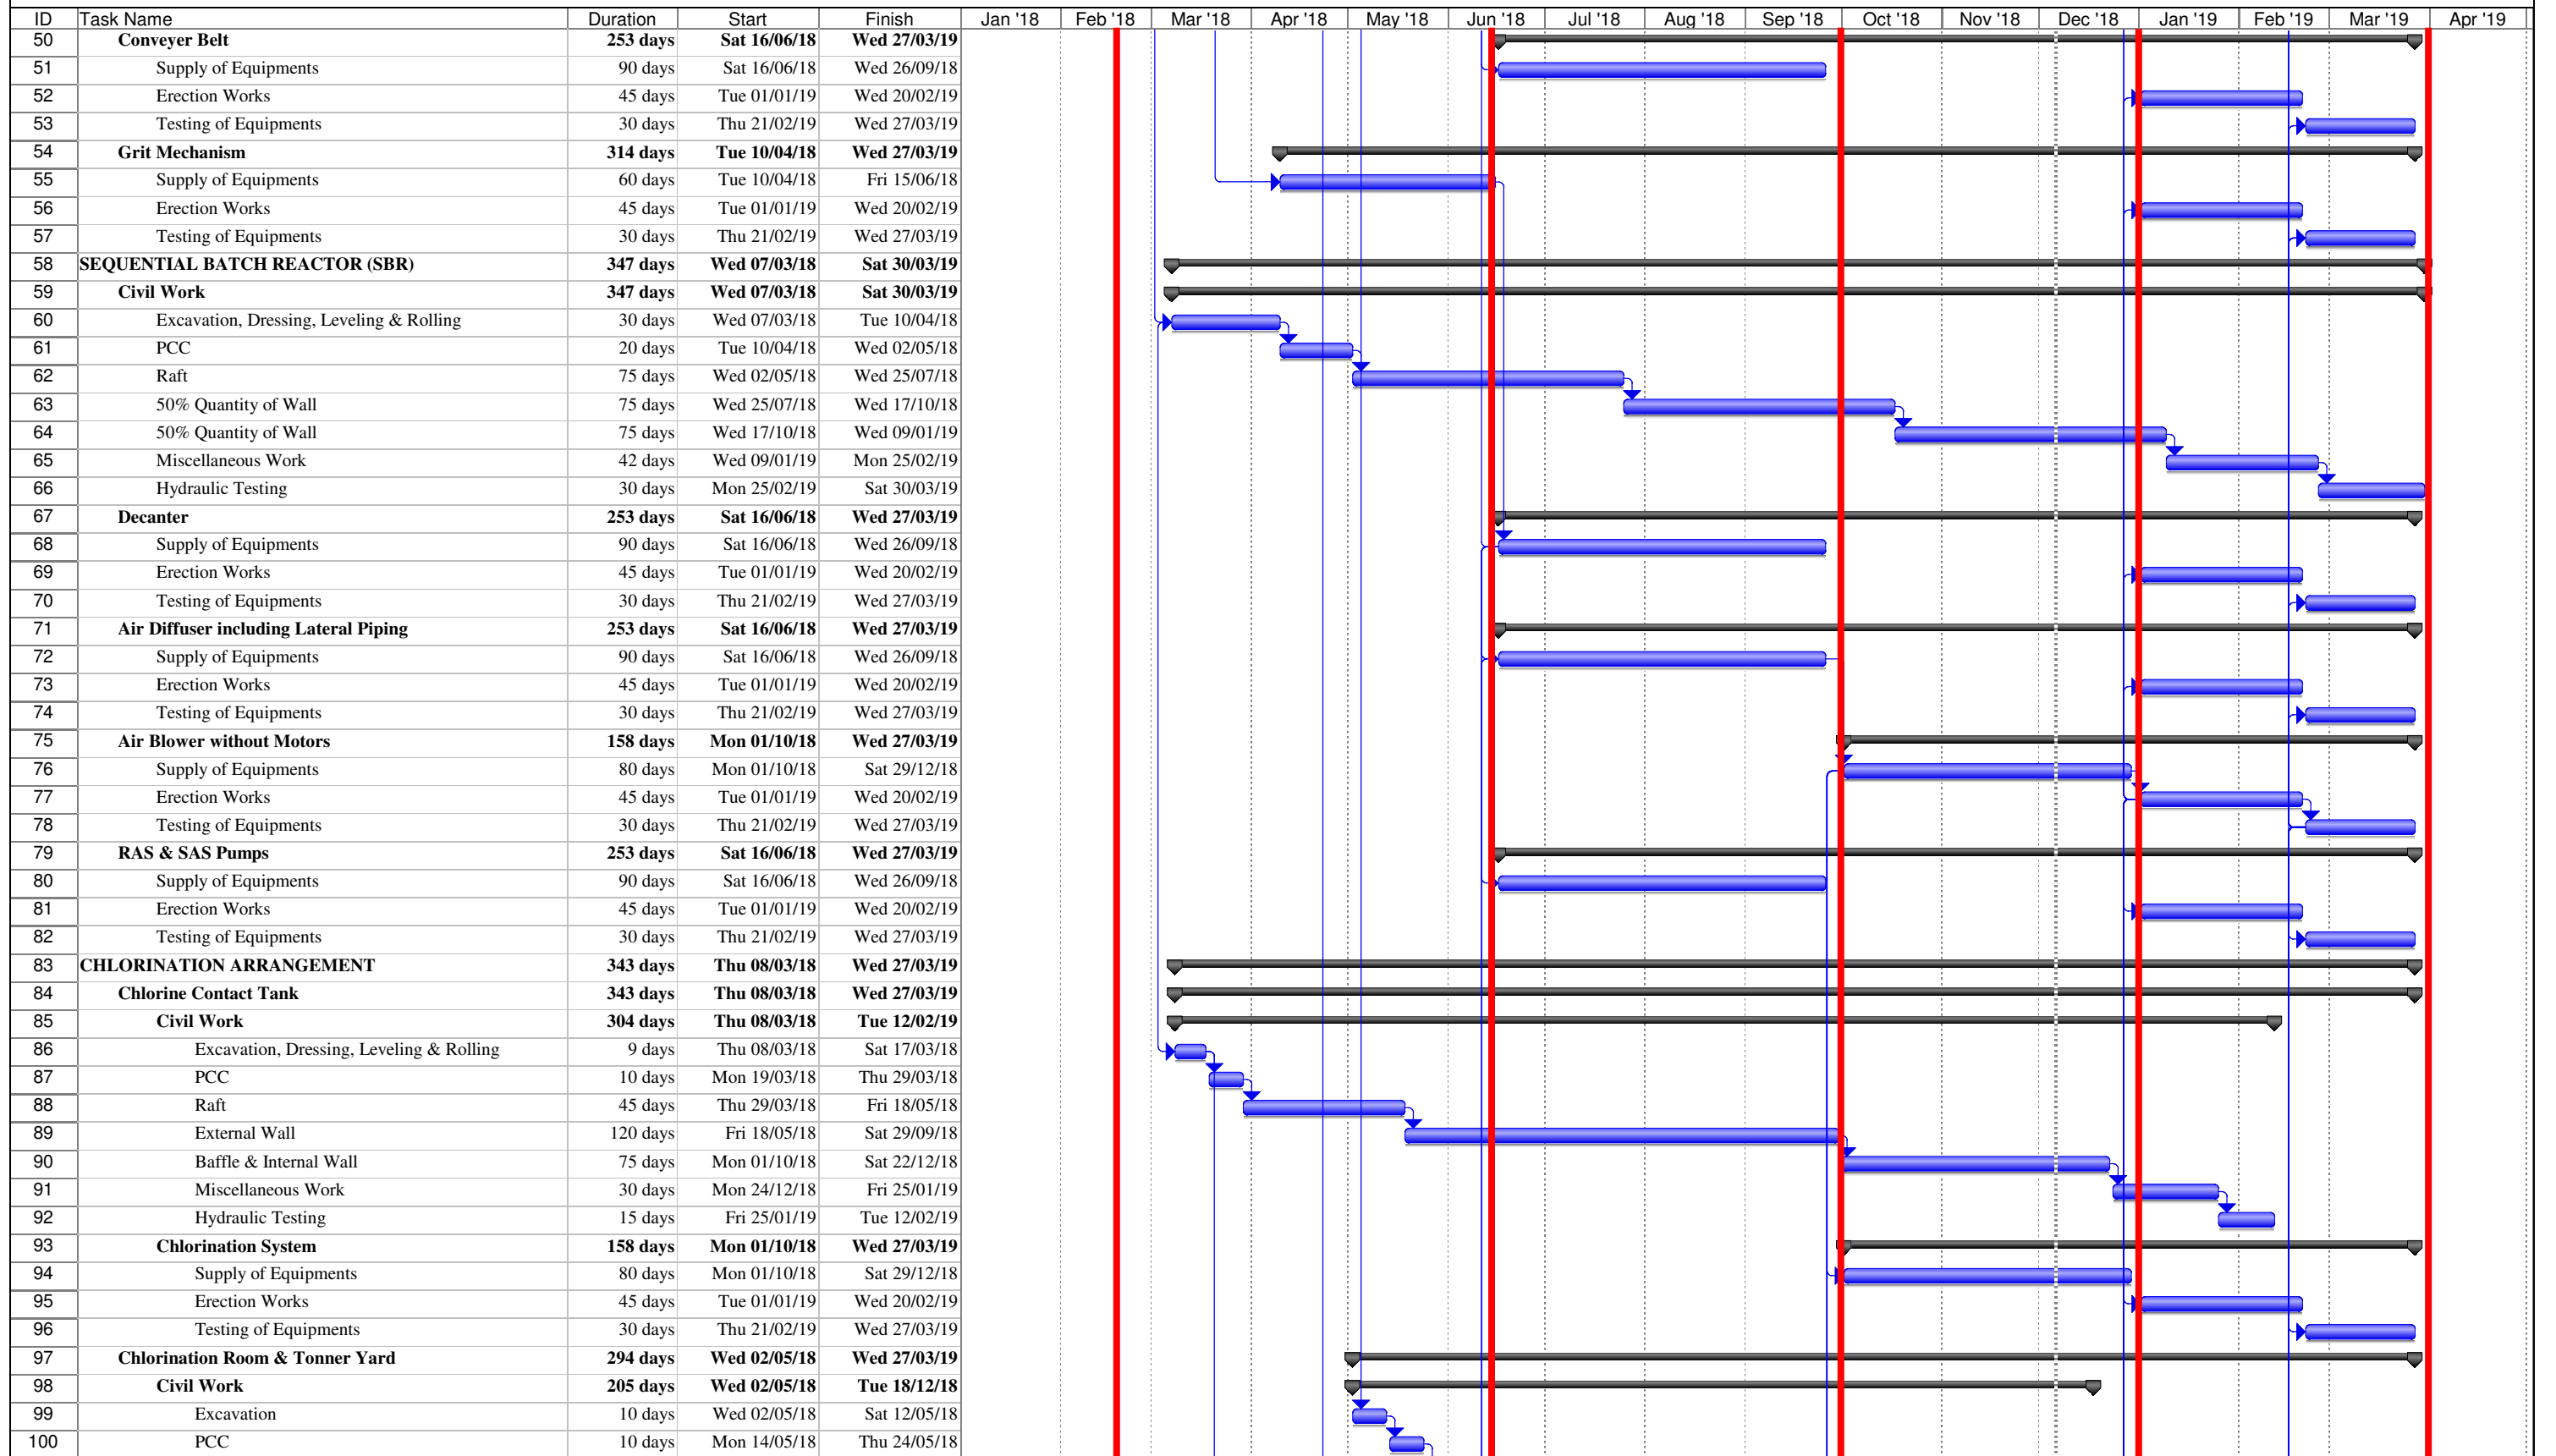

Project: 14 MLD STP@ SARAI HARIC
Date: Thu 06/12/18

Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

ID	Task Name	Duration	Start	Finish	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19
101	Column upto GL	20 days	Thu 24/05/18	Fri 15/06/18																
102	Column upto Roof Level	45 days	Fri 15/06/18	Sat 04/08/18																
103	Roof Slab	45 days	Mon 06/08/18	Tue 25/09/18																
104	Brick & Plastering Works	45 days	Tue 25/09/18	Wed 14/11/18																
105	Balance Civil Works	30 days	Wed 14/11/18	Tue 18/12/18																
106	Chlorine Tonner	158 days	Mon 01/10/18	Wed 27/03/19																
107	Supply of Equipments	50 days	Mon 01/10/18	Mon 26/11/18																
108	Erection Works	30 days	Mon 26/11/18	Sat 29/12/18																
109	Testing of Equipments	30 days	Thu 21/02/19	Wed 27/03/19																
110	SLUDGE DISPOSAL ARRANGEMENTS	334 days	Mon 19/03/18	Wed 27/03/19																
111	Sludge Thickner	260 days	Mon 19/03/18	Thu 03/01/19																
112	Excavation, Dressing, Leveling & Rolling	15 days	Mon 19/03/18	Wed 04/04/18																
113	PCC	15 days	Wed 04/04/18	Fri 20/04/18																
114	Raft	50 days	Fri 20/04/18	Fri 15/06/18																
115	50% Quantity of Wall	45 days	Fri 15/06/18	Sat 04/08/18																
116	50% Quantity of Wall	45 days	Mon 06/08/18	Tue 25/09/18																
117	Miscellaneous Work	30 days	Mon 29/10/18	Fri 30/11/18																
118	Hydraulic Testing	30 days	Fri 30/11/18	Thu 03/01/19																
119	Sludge Thickner Mechanism	253 days	Sat 16/06/18	Wed 27/03/19																
120	Supply of Equipments	90 days	Sat 16/06/18	Wed 26/09/18																
121	Erection Works	45 days	Mon 01/10/18	Wed 21/11/18																
122	Testing of Equipments	30 days	Thu 21/02/19	Wed 27/03/19																
123	Centrifuge Unit	270 days	Wed 04/04/18	Thu 31/01/19																
124	Excavation	15 days	Wed 04/04/18	Fri 20/04/18																
125	PCC	15 days	Fri 20/04/18	Tue 08/05/18																
126	Column upto GL	30 days	Tue 08/05/18	Sat 09/06/18																
127	Platform Slab	90 days	Mon 11/06/18	Wed 19/09/18																
128	Roof Slab	60 days	Wed 19/09/18	Sat 24/11/18																
129	Brick & Plastering Works	30 days	Mon 26/11/18	Fri 28/12/18																
130	Balance Civil Works	30 days	Fri 28/12/18	Thu 31/01/19																
131	Centrifuge	253 days	Sat 16/06/18	Wed 27/03/19																
132	Supply of Equipments	90 days	Sat 16/06/18	Wed 26/09/18																
133	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																
134	Testing of Equipments	30 days	Thu 21/02/19	Wed 27/03/19																
135	Centrifuge Feed Pump	158 days	Mon 01/10/18	Wed 27/03/19																
136	Supply of Equipments	80 days	Mon 01/10/18	Sat 29/12/18																
137	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																
138	Testing of Equipments	30 days	Thu 21/02/19	Wed 27/03/19																
139	Sludge Sump	225 days	Wed 04/04/18	Wed 12/12/18																
140	Excavation	15 days	Wed 04/04/18	Fri 20/04/18																
141	PCC	15 days	Fri 20/04/18	Tue 08/05/18																
142	Raft	30 days	Tue 08/05/18	Sat 09/06/18																
143	50% Quantity of Wall	30 days	Mon 11/06/18	Fri 13/07/18																
144	50% Quantity of Wall	30 days	Fri 13/07/18	Thu 16/08/18																
145	Miscellaneous Work	30 days	Fri 05/10/18	Thu 08/11/18																
146	Hydraulic Testing	30 days	Thu 08/11/18	Wed 12/12/18																
147	Sludge Sump Air Blower without Motors	158 days	Mon 01/10/18	Wed 27/03/19																
148	Supply of Equipments	80 days	Mon 01/10/18	Sat 29/12/18																
149	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																
150	Testing of Equipments	30 days	Thu 21/02/19	Wed 27/03/19																

Project: 14 MLD STP@ SARAI HARIC
Date: Thu 06/12/18


Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

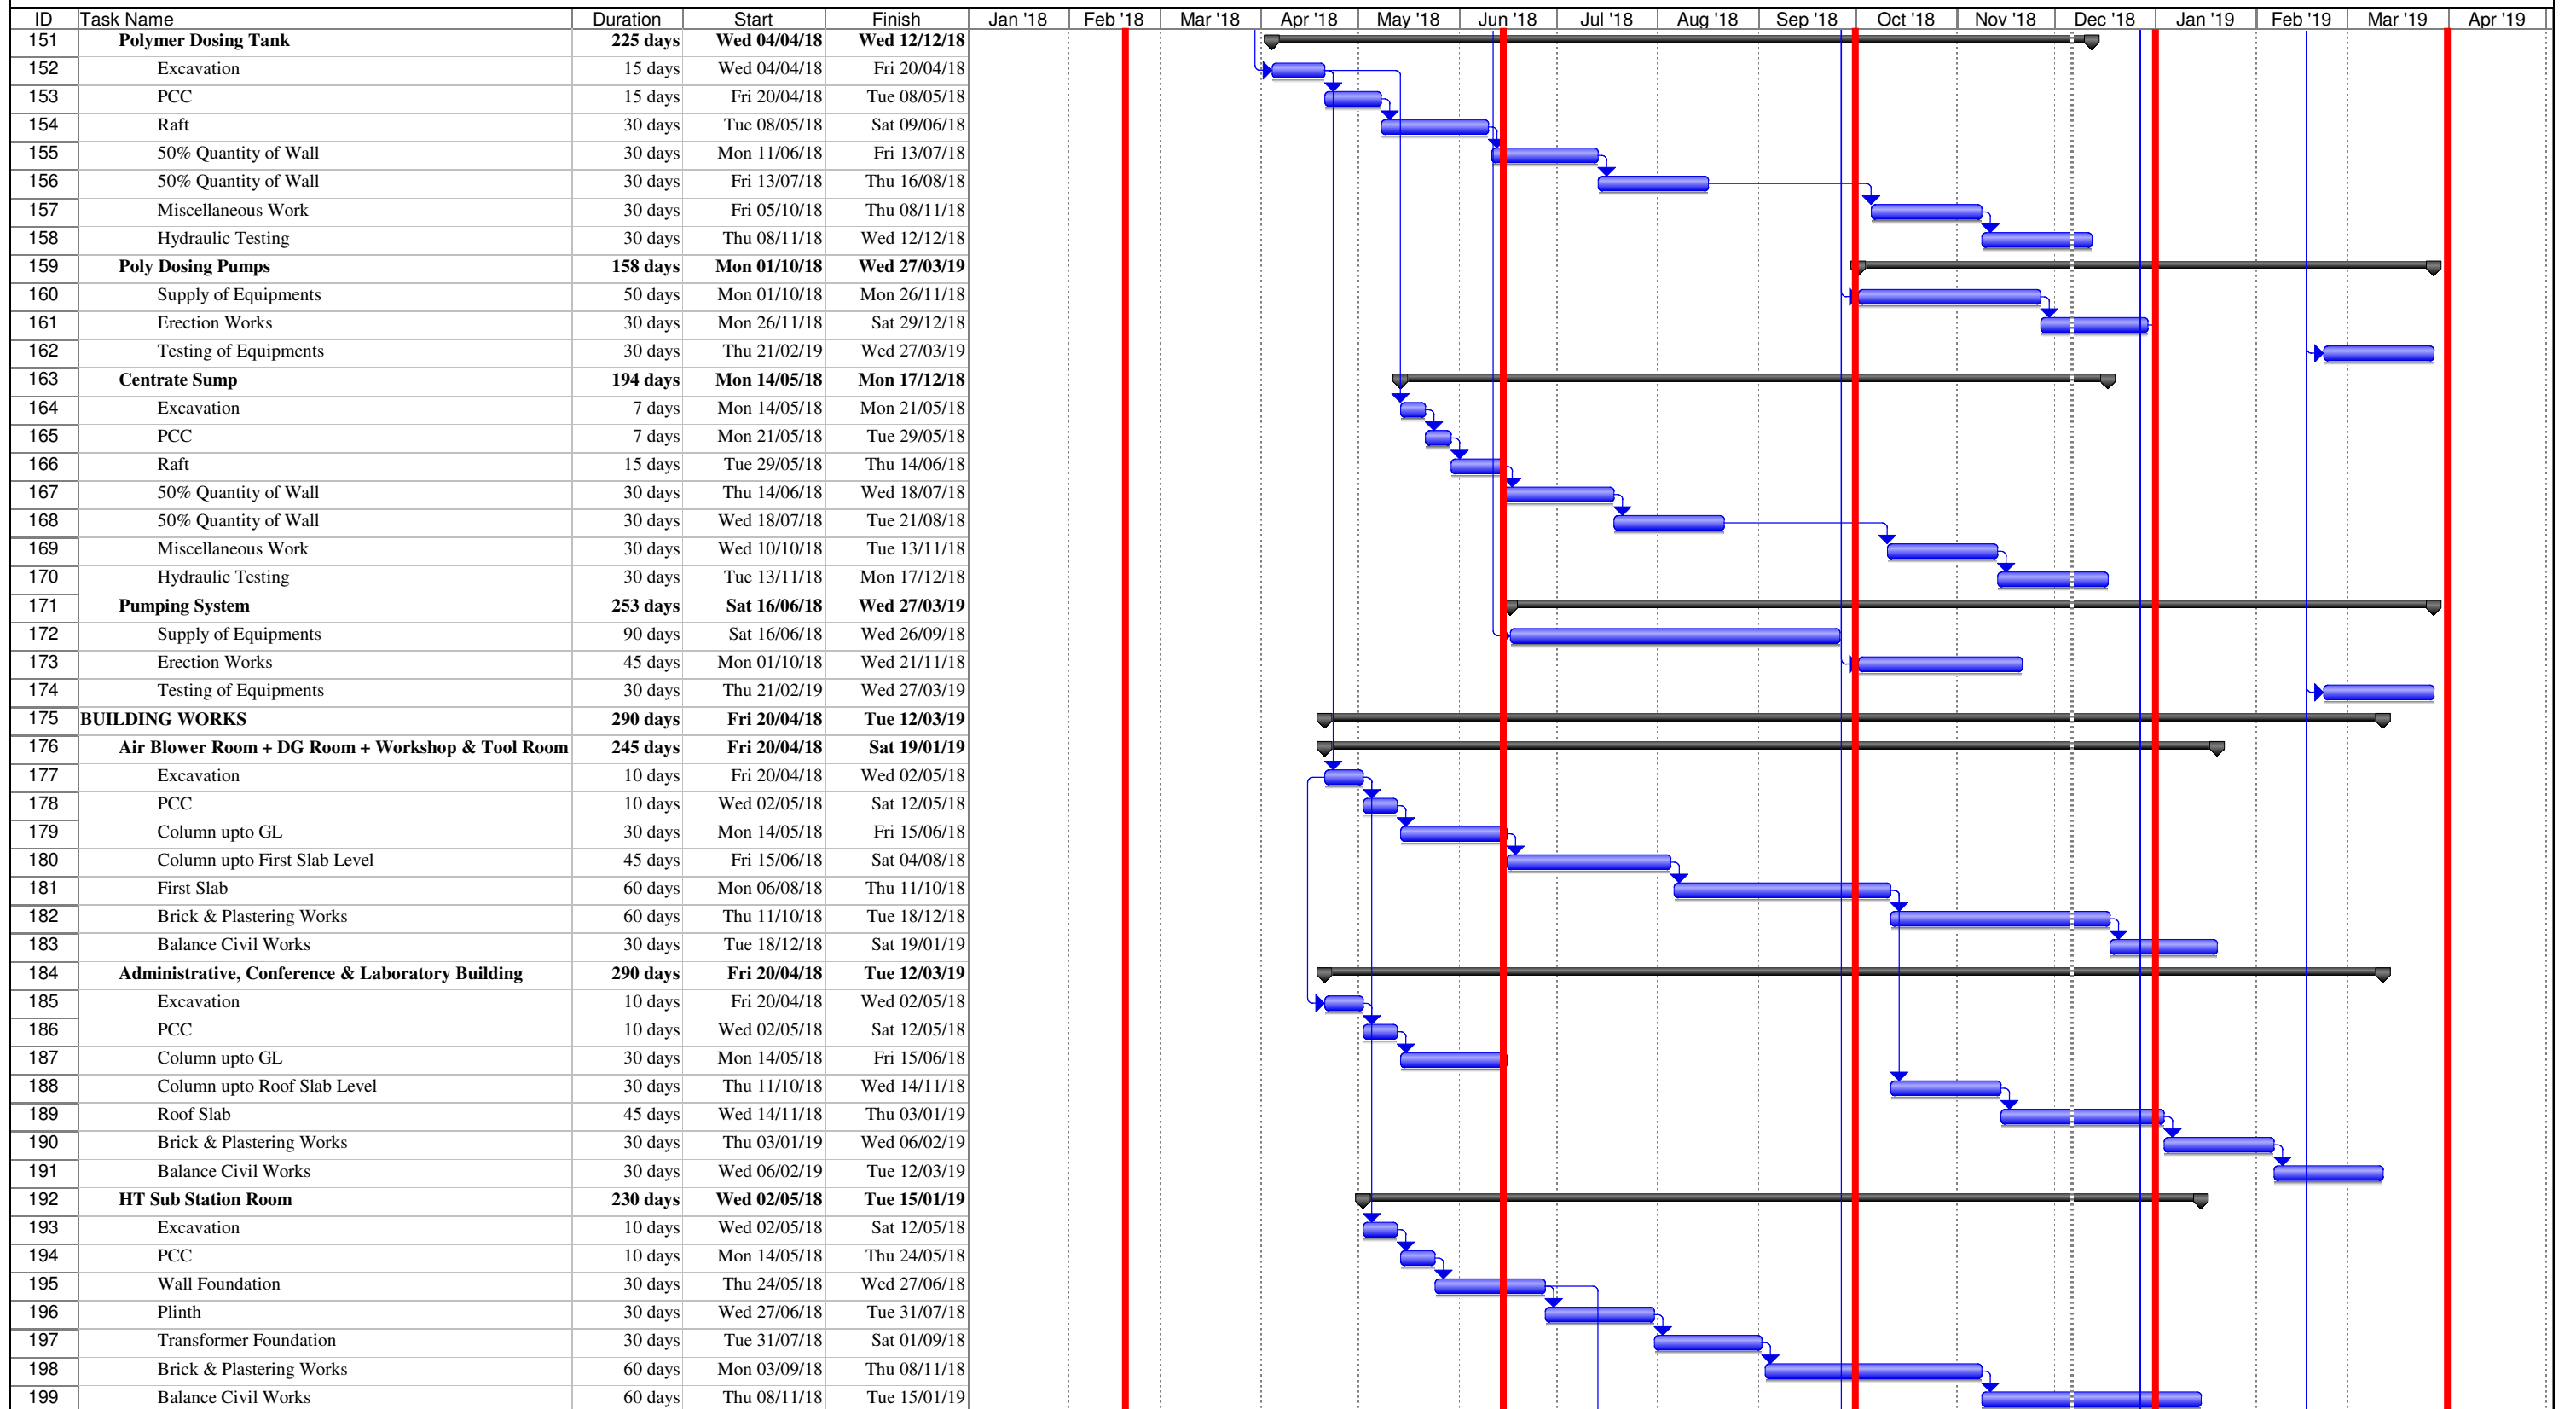

Project: 14 MLD STP@ SARAI HARIC
Date: Thu 06/12/18

Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

ID	Task Name	Duration	Start	Finish	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19	
200	Security Cabin	110 days	Fri 13/07/18	Wed 14/11/18																	
201	Excavation	5 days	Fri 13/07/18	Thu 19/07/18																	
202	PCC	5 days	Thu 19/07/18	Wed 25/07/18																	
203	Column upto GL	15 days	Wed 25/07/18	Fri 10/08/18																	
204	Column upto Slab Level	15 days	Fri 10/08/18	Tue 28/08/18																	
205	Slab	30 days	Tue 28/08/18	Sat 29/09/18																	
206	Brick & Plastering Works	20 days	Mon 01/10/18	Tue 23/10/18																	
207	Balance Civil Works	20 days	Tue 23/10/18	Wed 14/11/18																	
208	MISCELLANEOUS WORKS	153 days	Mon 01/10/18	Wed 20/03/19																	
209	Campus Road	70 days	Tue 01/01/19	Wed 20/03/19																	
210	Sub Base	20 days	Tue 01/01/19	Wed 23/01/19																	
211	WBM	30 days	Wed 23/01/19	Tue 26/02/19																	
212	Top Layer	20 days	Tue 26/02/19	Wed 20/03/19																	
213	Compound Wall	128 days	Mon 01/10/18	Wed 20/02/19																	
214	Excavation	10 days	Mon 01/10/18	Thu 11/10/18																	
215	PCC	7 days	Thu 11/10/18	Fri 19/10/18																	
216	Column Footing	15 days	Fri 19/10/18	Mon 05/11/18																	
217	Ground Beam	15 days	Mon 05/11/18	Thu 22/11/18																	
218	Brick & Plastering Works	15 days	Thu 22/11/18	Sat 08/12/18																	
219	Miscellaneous Work	20 days	Sat 08/12/18	Mon 31/12/18																	
220	Balance Civil Works	45 days	Tue 01/01/19	Wed 20/02/19																	
221	Landscaping, Site Development & Plantation	40 days	Tue 01/01/19	Fri 15/02/19																	
222	Landscaping	20 days	Tue 01/01/19	Wed 23/01/19																	
223	Horticulture Development	20 days	Wed 23/01/19	Fri 15/02/19																	
224	ELECTRICAL & INSTRUMENTATION WORKS	158 days	Mon 01/10/18	Wed 27/03/19																	
225	Transformer	158 days	Mon 01/10/18	Wed 27/03/19																	
226	Supply of Machinery / Equipments at Site	80 days	Mon 01/10/18	Sat 29/12/18																	
227	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																	
228	Testing of Equipment	30 days	Thu 21/02/19	Wed 27/03/19																	
229	DG	76 days	Tue 01/01/19	Wed 27/03/19																	
230	Supply of Machinery / Equipments at Site	30 days	Tue 01/01/19	Mon 04/02/19																	
231	Erection Works	15 days	Mon 04/02/19	Wed 20/02/19																	
232	Testing of Equipment	30 days	Thu 21/02/19	Wed 27/03/19																	
233	LT Panel	76 days	Tue 01/01/19	Wed 27/03/19																	
234	Supply of Machinery / Equipments at Site	30 days	Tue 01/01/19	Mon 04/02/19																	
235	Erection Works	15 days	Mon 04/02/19	Wed 20/02/19																	
236	Testing of Equipment	30 days	Thu 21/02/19	Wed 27/03/19																	
237	Cable & Cable Tray	158 days	Mon 01/10/18	Wed 27/03/19																	
238	Supply of Machinery / Equipments at Site	80 days	Mon 01/10/18	Sat 29/12/18																	
239	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																	
240	Testing of Equipment	30 days	Thu 21/02/19	Wed 27/03/19																	
241	PLC / SCADA System	158 days	Mon 01/10/18	Wed 27/03/19																	
242	Supply of Machinery / Equipments at Site	80 days	Mon 01/10/18	Sat 29/12/18																	
243	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																	
244	Testing of Equipment	30 days	Thu 21/02/19	Wed 27/03/19																	
245	Motors for Air Blowers	158 days	Mon 01/10/18	Wed 27/03/19																	
246	Supply of Machinery / Equipments at Site	80 days	Mon 01/10/18	Sat 29/12/18																	
247	Erection Works	45 days	Tue 01/01/19	Wed 20/02/19																	
248	Testing of Equipment	30 days	Thu 21/02/19	Wed 27/03/19																	

Project: 14 MLD STP@ SARAI HARIC
Date: Thu 06/12/18

Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone



HNB ENGINEERS (HARIDWAR) PVT. LTD.

SPV OF HNB ENGINEERS PVT. LTD.

Engineers & Turnkey Contractors

ID	Task Name	Duration	Start	Finish	Jan '18	Feb '18	Mar '18	Apr '18	May '18	Jun '18	Jul '18	Aug '18	Sep '18	Oct '18	Nov '18	Dec '18	Jan '19	Feb '19	Mar '19	Apr '19
249	INTERCONNECTING PIPING & PIPE FITTINGS WORKS	157 days	Mon 01/10/18	Tue 26/03/19																
250	RCC Pipes Works	157 days	Mon 01/10/18	Tue 26/03/19																
251	Supply of Material	80 days	Mon 01/10/18	Sat 29/12/18																
252	Excavation	30 days	Tue 01/01/19	Mon 04/02/19																
253	Lowering & Laying	45 days	Mon 04/02/19	Tue 26/03/19																
254	CI & DI Pipes Works	157 days	Mon 01/10/18	Tue 26/03/19																
255	Supply of Material	80 days	Mon 01/10/18	Sat 29/12/18																
256	Excavation	30 days	Tue 01/01/19	Mon 04/02/19																
257	Lowering & Laying	45 days	Mon 04/02/19	Tue 26/03/19																
258	Valves & Specials	75 days	Tue 01/01/19	Tue 26/03/19																
259	Supply of Material	30 days	Tue 01/01/19	Mon 04/02/19																
260	Excavation	15 days	Mon 04/02/19	Wed 20/02/19																
261	Lowering & Laying	30 days	Wed 20/02/19	Tue 26/03/19																

1. Activities shown above may start and finish earlier / later depending on site condition
2. Progress at Site is dependent on timely payment of advance and bill
3. Above Bar Chart is excluding monsoon period

Project: 14 MLD STP@ SARAI HARIC
Date: Thu 06/12/18

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			
